
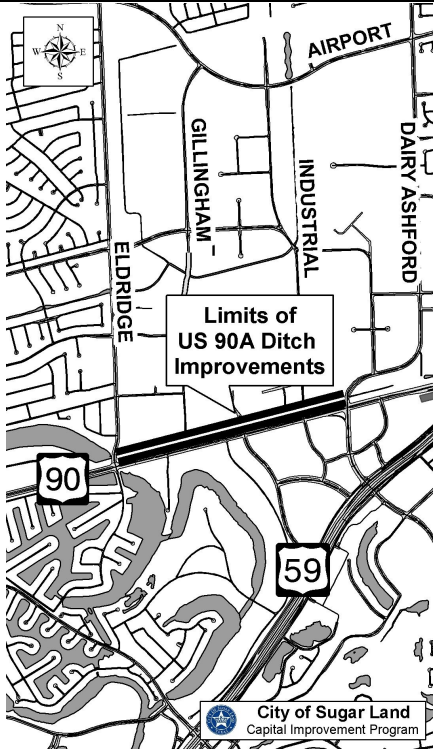


CAPITAL IMPROVEMENT PROGRAM 2008 PROJECT SCHEDULE

PROJECT No.				DR0602		PROJECT DESCRIPTION Design and construction of drainage improvements in US90A Ditch Watershed. The watershed drains to the 90A Ditch located between the limits of Eldridge Rd. and Dairy Ashford. This project is to mitigate existing flooding conditions and to accommodate development of the remaining undeveloped tracts within the 90A watershed.
PROJECT TITLE				US 90A DITCH IMPROVEMENTS		
PROJECT STATUS				DESIGN PHASE		
PROJECT MANAGER				SHASHI KUMAR		
CONSULTANT				DANNENBAUM ENGINEERING		
CONTRACTOR						
BUDGET				170,000		
PROJECT SCHEDULE		PROJECTED INITIATE - FINISH	REVISED INITIATE - FINISH	ACTUAL INITIATE - FINISH	PROGRESS PHOTO 	
PER *		08/06 – 12/06		08/06 – 02/07		
LAND/ROW **						
DESIGN/SURVEYING		03/07 – 03/08				
CONSTRUCTION						
EQUIPMENT						
SCHEDULE COMMENTS						

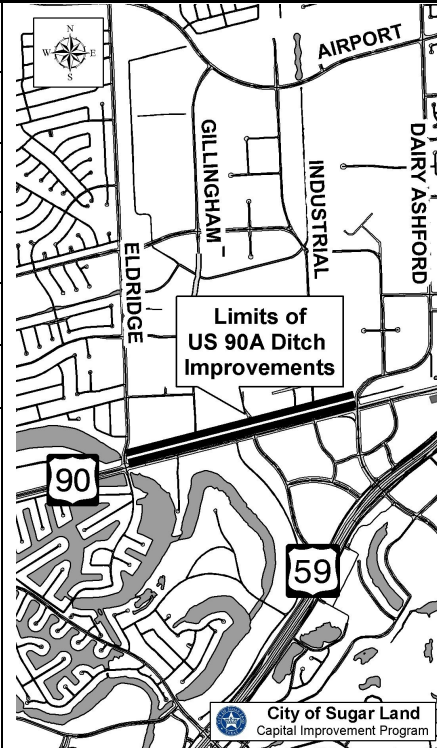

*PER = Preliminary Engineering Report

**ROW = Right-of-Way
