


CAPITAL IMPROVEMENT PROGRAM 2008 PROJECT SCHEDULE

PROJECT No.		DR0704		PROJECT DESCRIPTION
PROJECT TITLE		LOCALIZED DRAINAGE IMPROVEMENTS		
PROJECT STATUS		CONSTRUCTION PHASE		
PROJECT MANAGER		GREG NICHOLS		
CONSULTANT		KELLY KALUZA & ASSOCIATES, KSA ENGINEERS		
CONTRACTOR		FORT BEND EXCAVATION		
BUDGET		\$250,000		
PROJECT SCHEDULE	PROJECTED INITIATE - FINISH	REVISED INITIATE - FINISH	ACTUAL INITIATE - FINISH	PROGRESS PHOTO
PER *				
LAND/ROW **				
DESIGN/SURVEYING	10/06 – 02/07		10/06 – 02/07	
CONSTRUCTION	04/07- 11/07			
EQUIPMENT				
SCHEDULE COMMENTS				

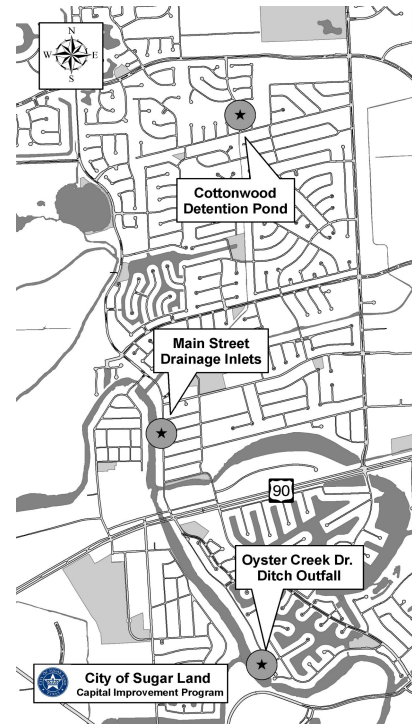

*PER = Preliminary Engineering Report

**ROW = Right-of-Way
