
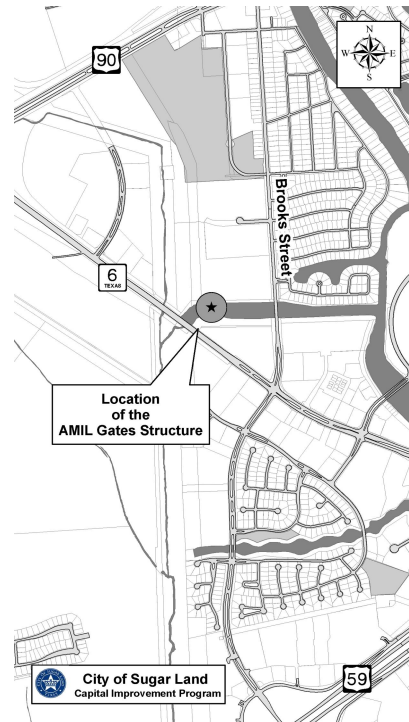


CAPITAL IMPROVEMENT PROGRAM 2008 PROJECT SCHEDULE

PROJECT NO.		DR0705		PROJECT DESCRIPTION
PROJECT TITLE		AMIL GATES REHABILITATION		
PROJECT STATUS		DESIGN PHASE		
PROJECT MANAGER		GREG NICHOLS		
CONSULTANT		PATE ENGINEERS		
CONTRACTOR				
BUDGET		\$240,000		
PROJECT SCHEDULE	PROJECTED INITIATE - FINISH	REVISED INITIATE - FINISH	ACTUAL INITIATE - FINISH	PROGRESS PHOTO
PER *	02/07 – 04/07		02/07 – 04/07	
LAND/ROW **				
DESIGN/SURVEYING	04/07 – 10/07			
CONSTRUCTION	TBD			
EQUIPMENT				
SCHEDULE COMMENTS				

<p>AMIL Gates located across Brooks Lake Diversion Channel mainly serve as flood control gates and also facilitate maintaining constant water surface elevation upstream of the gates.</p>				
				



*PER = Preliminary Engineering Report

**ROW = Right-of-Way
