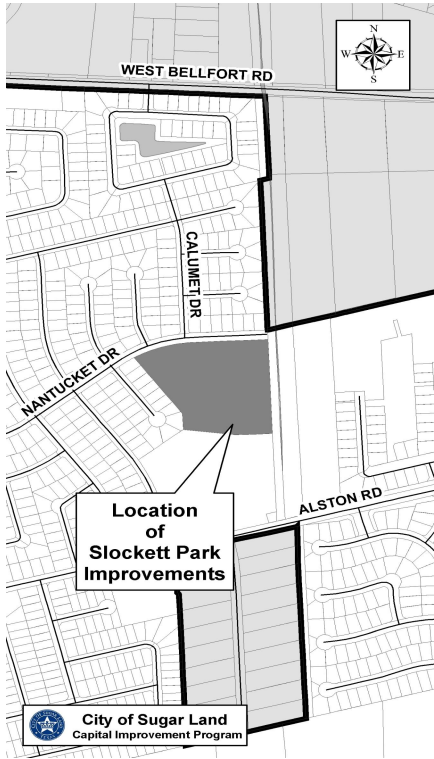


## CAPITAL IMPROVEMENT PROGRAM 2008 PROJECT SCHEDULE

PROJECT NO.		PK0710		PROJECT DESCRIPTION	Security lighting and conversion of existing basketball court to a picnic pavilion.
PROJECT TITLE		SLOCKETT PARK IMPROVEMENTS			
PROJECT STATUS		CONSTRUCTION PHASE			
PROJECT MANAGER		KIM TERRELL			
CONSULTANT					
CONTRACTOR					
BUDGET		\$60,000			
PROJECT SCHEDULE	PROJECTED INITIATE - FINISH	REVISED INITIATE - FINISH	ACTUAL INITIATE - FINISH		PROGRESS PHOTO
PER *					
LAND/ROW **					
DESIGN/SURVEYING	01/07 – 03/07		01/07 – 03/07		
CONSTRUCTION	10/07 – 01/08				
EQUIPMENT					
SCHEDULE COMMENTS					

\*PER = Preliminary Engineering Report

\*\*ROW = Right-of-Way
