## CAPITAL IMPROVEMENTS PROGRAM 2003 PROJECT SCHEDULE

PROJECT TITLE: ST0204 Bridge Slope Paving – Austin Parkway @ Ditch "E" and Sweetwater @ Ditch "A" South Crossing

<u>DESCRIPTION</u>: Design and construction of approximately 2000 square yards of concrete slope paving under bridge crossings located at Austin Parkway @ Ditch "E" and Sweetwater @ Ditch "A" South Crossing.

Rudget

## **PROJECT MANAGER:**

Ross Woodfin, Project Manager

**BUDGET SOURCE**: General Revenue

**BUDGET AMOUNT:** \$150,000


## **BUDGET LINE ITEM (S):**

	<u> Duuget</u>
Design	\$ 13,000
Topographical Survey	3,500
Geotechnical Study	3,000
Construction	115,000
Materials Testing	2,000
Contingency	13,500
Total	\$150,000

**CONSULTANT (S)**: Brooks and Sparks

**CONTRACTOR (S)**:

**COMPLETED PROJECT TOTAL:** 

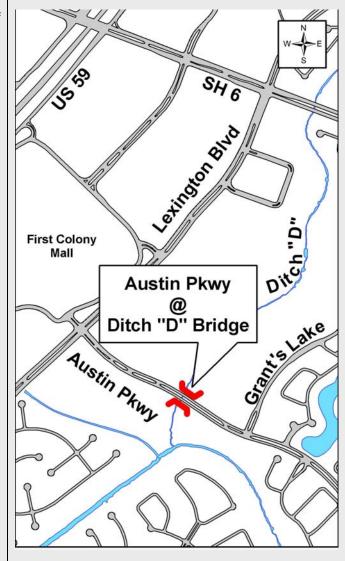

PROJECT SCHEDULE:	Proposed	Revised	Actual
	Date	Date	Date

 Design
 01/02 - 05/02
 07/02 - 6/03

 Construction
 05/02 - 09/02
 08-03 - 10/03

(FY 02 Preliminary Engineering construction estimates indicate a funding shortfall. Sweetwater location deferred after site assessments).
